

User Manual of

Sagar Manthan Projects

Prepared By
NTCPWC, IITM
June, 2024

Contents

1	Introduction	2
1.1	Purpose of this document	2
1.2	Intended Audience	2
1.3	Project Background	2
2	Projects Module	2
2.1	Projects	2
2.2	Add Projects	3
2.3	Add Sub Projects	3
3	Planning and Sanctioning (Port User)	4
4	Planning and Sanctioning (Ministry User)	6
5	Clearance	8
6	Under Tendering	9
7	Under Implementation	12
8	Project Completion	17
9	Drop a Project	17
10	Reports	19
10.1	Report No.: P.1.0 - Abstract - Status of Planning Sanctioning of Projects	19
10.2	Report No.: P.1.1A - Abstract - Status of Planning Sanction of Projects	19
10.3	Report No.: P.1.2A - Abstract - Status of Projects under Tendering . .	20
10.4	Report No.: P.1.3A - Abstract - Status of Implementation of Projects .	21
10.5	Report No.: P.1.4A - Abstract - Status of Physical and Financial Status of Projects	22
11	Validations and Conditions - Projects	23
11.1	Basic Information	23
11.2	Planning and Sanctioning	23
11.3	Note	24
11.4	Clearances	24
11.5	Under Tendering	24
11.6	Under Implementation	24
12	Amendment Details	25
13	Distribution List & Contact Details	25

1 Introduction

1.1 Purpose of this document

The purpose of this document is to describe business requirements of ‘Sagar Manthan’ Dashboard completely, accurately and unambiguously in Technology-independent manner. All attempts have been made in using mostly business terminology and business language while describing the requirements in this document. Very minimal and commonly understood Technical terminology is used. Use case / Designer approach is used in modeling the business requirements in this document.

1.2 Intended Audience

The main intended audience for this document are Ministry of Ports , Shipping and Waterways. This document should be readable by business owners of the proposed system. They must be able to verify that their business requirements have been documented here completely, accurately and unambiguously.

Data Architects, Application Architects and Technical Architects would also find the information in this document useful when they need to design a solution that will address these business requirements.

Since the requirements are documented here in Technology-independent manner, the end-users of the system should be able to comprehend the requirements fairly easily from this document.

1.3 Project Background

The newly ‘Sagar Manthan’ dashboard is expected to enhance the functioning of different departments by providing well-coordinated and up-to-date information in real-time. ***The Ministry of Ports***, Shipping and Waterways has demonstrated its commitment to promoting the growth of India’s maritime transport sector by launching the ‘Sagar Manthan’ Dashboard, which represents a step towards digitization and transparency in the sector.

2 Projects Module

The Projects and Proposals are combined into a single module in this version of SagarManthan.

2.1 Projects

The Projects button takes you to a page listing the current Projects their updating options and a button to add new projects. The current stages of the different projects like DPR,Under Tendering, Completed etc are displayed here as shown below.

S.No	Project Id	Sub Project ID	Project Name	Sub Project Name	Sanctioned Cost (In Cr.)	Primary Implementing Agency	Current Stage	Edit
1	PR0653	-	tywetw	-		Andhra Pradesh Tourism Development Corporation	Project Initiated	Update
2	PR0459	-	Upgradation of existing 80 bedded Golden Jubilee hospital to a 300 bedded Multi-Disciplinary Super Speciality Hospital through PPP Mode at Visakhapatnam Port on Design, Build, Finance, Operate and Transfer (DBFOT) Basis.	-	263.82	Visakhapatnam Port Authority	DPR	Update
3	PR0071	-	Revamping of existing West Quay-6 terminal in the Northern arm of Inner Harbor of Visakhapatnam Port for handling	-	165.70	Visakhapatnam Port Authority	Under Tendering	Update

Figure 1: Project Listing

2.2 Add Projects

The Add project option takes you to a Basic data entry page like below. Please note that depending on the project type the further entry page varies. For all Project types other than Port Level Approval further entries are to be done by the Ministry user. In the case of choosing the Port Level Approval the subsequent data entry is to be done by the Normal user itself as the further Stage (Planning and Sanctioning) needs Board Chairman approval.

Figure 2: Add Projects

2.3 Add Sub Projects

The Data form has an option to enter sub projects if any. Depending on the number of sub projects the data form allows an input field for sub project names.

The Projects input data form allows the save option only after the mandatory fields marked as *, are entered. After saving the project data form, the list of projects are displayed where the recently created projects are displayed.

Figure 3: Add Sub Projects

The newly created project with the basic information entered will be listed as shown below . The Update button can be used to proceed to subsequent stages.

S.No	Project Id	Sub Project ID	Project Name	Sub Project Name	Sanctioned Cost (In Cr.)	Primary Implementing Agency	Current Stage	Edit
1	PR0459	-	Upgradation of existing 80 bedded Golden Jubilee hospital to a 300 bedded Multi-Disciplinary Super Speciality Hospital through PPP Mode at Visakhapatnam Port on Design, Build, Finance, Operate and Transfer (DBFOT) Basis.	-	263.82	Visakhapatnam Port Authority	DPR	Update
2	PR0071	-	Revamping of existing West Quay-6 terminal in the Northern arm of Inner Harbor of Visakhapatnam Port for handling of dry bulk cargo on DBFOT basis.	-	165.70	Visakhapatnam Port Authority	Under Tendering	Update

Figure 4: Update option for Newly added project

3 Planning and Sanctioning (Port User)

The Update option then takes you to the next step which is the Planning and Sanctioning stage. The data form of the next stage which is the Planning and Sanctioning depends on whether the port user has chosen Port Level approval or not. If the Port Level Approval is chosen then the Port user need to do the updating for the Chairman level Approval data as shown below.

Kakinada

Land Detail

Is Land Acquisition required for Project?

☐ Yes
☒ No

Percent of Land Acquired

Others

Project PPT

NOTE: Multiple PDF file can be uploaded. File Size: Max. 10 MB.

Upload

Drag & Drop Files

PERT Chart

NOTE: Multiple PDF file can be uploaded. File Size: Max. 10 MB.

Upload

Drag & Drop Files

Latest Project Image

NOTE: Multiple images can be uploaded.

Upload

Drag & Drop Files

Update

Drop

Exit

View Uploaded Documents

Next

Figure 5: Land Acquisition Option

On Choosing Yes for Land Acquisition the details of land Acquired is to be entered.

Land Detail

Is Land Acquisition required for Project?

☒ Yes
☐ No

Land Area Required (In Hectare)

Is the Acquisition completed?

☐ Yes
☒ Not Yet

Percent of Land Acquired

Others

Project PPT

NOTE: Multiple PDF file can be uploaded. File Size: Max. 10 MB.

Upload

Drag & Drop Files

PERT Chart

NOTE: Multiple PDF file can be uploaded. File Size: Max. 10 MB.

Upload

Drag & Drop Files

Latest Project Image

NOTE: Multiple images can be uploaded.

Upload

Drag & Drop Files

Update

Drop

Exit

View Uploaded Documents

Next

Figure 6: Land Acquisition Details

There is an option to save the data using the Update Button at this stage. The Port User need to the move to the NEXT data entry page of planning and sanctioning.

Planning and sanctioning page which will have the Chairman board approval with only four fields, Pre-feasibility date ,DPR date,Sanctioned cost and Chairman approval date. Date of approval by Chairman and sanctioned cost is compulsory entry to go to next stage. After the Mandatory data is entered the Port User reaches the next stage which is the Clearance stage which is optional or can also be done later also. Please note that the subsequent stages are common for both Port Users (Project type is Port Level Approval) and the Ministry users.

Planning and Sanctioning

Stages	Actual Date*	Remarks
Preliminary-Feasibility (Note: To be filled by organisation users)	dd-mm-yyyy ☐	
DPR (Note: To be filled by organisation users)	dd-mm-yyyy ☐	
Chairman Board Approval (Note: To be filled by organisation users)		
Sanctioned Cost (In Cr) 	dd-mm-yyyy ☐	

[Save](#) [Exit](#) [Previous](#) [Next](#)

Figure 7: To Planning and Sanctioning Page

4 Planning and Sanctioning (Ministry User)

If the Project Type is anything other than Port Level Approval is chosen then the Ministry user need to do the rest of the processes by initiating the **Update** button. You may note that when the ministry user logs in there is no button for add projects , Adding a new Project can be done only by the port User

Project List

Filters

Export All Data

Show 10 entries

Search:

S.No	Project ID	Sub Project ID	Project Name	Sub Project Name	Sanctioned Cost (In Cr)	Primary Implementing Agency	Current Stage	Edit
1	PR0654	-	MAINTENANCE DREDGING OF PARADIP PORT AUTHORITY(2024-2025)	-		Chennai Port Authority	Project Initiated	Update
2	PR0652	-	Providing Shore Protection at Jawahar Dweep	-		Mumbai Port Authority	Project Initiated	Update
3	PR0636	-	Rehabilitation of Bascule Bridge at KDS, SMPK	-	0.28	Syama Prasad Mookerjee Port	Project Initiated	Update
4	PR0139	-	Coastal berth with dredged depth of 10.0m to handle vessels up to 15000 DWT -length 150m at VoCPT	-	36.00	Mormugao Port Authority	Pre-Feasibility	Update

Figure 8: Project Listing of a Ministry User

The update buttons takes you to the Basic Information page of the Project . Except the Project ID the ministry user can update all the fields if needed. The * fields are as always mandatory

clouds.ntpcwct.in:49/sagarmanthan/pages/ProjectManagement/editProject.html?project_id=PR0654&sub_project_id=1

GOVERNMENT OF INDIA | MINISTRY OF PORTS, SHIPPING AND WATERWAYS

BETA Version 1.1

Project List View Drop Request Reports

1 Basic Information 2 Planning and Sanctioning 3 Clearances 4 Under Tendering 5 Under Implementation 6 Project Completion

Basic Information

General Details

Project ID *
PRO654

Sub Project ID *

Project Name *
MAINTENANCE DREDGING OF PARADIP PORT AUTHORITY(2024-2025)

Project Brief *
erer

Estimated Cost (In Cr.) *
1234567890

Project Type *
PIB

Implementation Type *
Single Funded

Project Category *
xBerth

Figure 9: Planning and Sanctioning Update Page

Bottom of the basic information , the necessary supporting documents like PPT presentations , Charts or related photographs can be uploaded and can press **Next** for subsequent data entry in Planning and Sanctioning

MP Constituency*
Gulbarga

Land Detail

Is Land Acquisition required for Project?
☐ Yes ☒ No

Percent of Land Acquired

Others

Project PPT
NOTE: Multiple PDF file can be uploaded. File Size: Max. 10 MB.
 Drag & Drop Files

PERT Chart
NOTE: Multiple PDF file can be uploaded. File Size: Max. 10 MB.
 Drag & Drop Files

Latest Project Image
NOTE: Multiple images can be uploaded.
 Drag & Drop Files

[View Uploaded Documents](#)

Figure 10: Planning and Sanctioning Document Upload

In the following page the user has to enter the actual dates of Preliminary Feasibility , DPR , IMC circulation and Approval and many more entries as shown below.

Project List	View Drop Request	Reports
DPR (Note: To be filled by organisation users)	dd-mm-yyyy	
Submitted to Ministry (Note: To be filled by organisation users)	dd-mm-yyyy	
DA concurrence obtained	dd-mm-yyyy	
IFW concurrence obtained	dd-mm-yyyy	
Circulated for IMC - Circulation	dd-mm-yyyy	
Circulated for IMC - Approval	dd-mm-yyyy	
Response to Comments Received	dd-mm-yyyy	
Approved by SFC/DIB/EFC/PIB/DIB/PPPAC	dd-mm-yyyy	
Admn. Approval/Estimate Sanction by Comp. Authority (Note: To be filled by organisation users)	dd-mm-yyyy	
Sanctioned Cost (In Cr)		

Copyright © 2024 Ministry of Ports, Shipping and Waterways, Government of India. All Rights Reserved.

Figure 11: Actual Approval dates of various events

5 Clearance

This step in Projects is completely optional as only if a particular project requires any clearance out of the mentioned list box clearances, then the port user need to enter their details and any supporting document can be uploaded.

Figure 12: Clearances Data entry

The clearance details if entered will be displayed as below

Sl. No.	Clearance Required	Applied Date	Received Date	Clearance Document	Edit
1	Archaeological Survey of India (ASI) Clearances	2024-06-08	2024-06-06	Download	

Figure 13: Clearances Data Listing

6 Under Tendering

After documents for clearance is uploaded the next step is Tendering . In this step the Tech. Sanctioned cost and the Awarded Project Costs are the compulsory data along with all the actual dates of the various events.

There is also provision to revise the Target Completion Date as shown below.

1 Basic Information
2 Planning and Sanctioning
3 Clearances
4 Under Tendering
5 Under Implementation
6 Project Completion

Under Tendering

Number of Tender Calls till Date

	Targeted Completion Date	Revision			Actual Date*
		Revised Date	Revise	History	
Tech. Sanction obtained NOTE: Only One PDF file can be uploaded. File Size: Max. 10 MB.					
Tech. Sanction Cost (In Cr) * 	dd-mm-yyyy	dd-mm-yyyy			dd-mm-yyyy
Tender Document approved NOTE: Only One PDF file can be uploaded. File Size: Max. 10 MB.	dd-mm-yyyy	dd-mm-yyyy			dd-mm-yyyy
Tender Notice Issued NOTE: Only One PDF file can be uploaded. File Size: Max. 10 MB.	dd-mm-yyyy	dd-mm-yyyy			dd-mm-yyyy

Figure 14: Under Tendering Data - 1

Tender Notice Issued NOTE: Only One PDF file can be uploaded. File Size: Max. 10 MB.	dd-mm-yyyy	dd-mm-yyyy			dd-mm-yyyy
Technical Evaluation completed NOTE: Only One PDF file can be uploaded. File Size: Max. 10 MB.	dd-mm-yyyy	dd-mm-yyyy			dd-mm-yyyy
Financial Evaluation completed NOTE: Only One PDF file can be uploaded. File Size: Max. 10 MB.	dd-mm-yyyy	dd-mm-yyyy			dd-mm-yyyy
Sanction of Competent Authority obtained for Award NOTE: Only One PDF file can be uploaded. File Size: Max. 10 MB.	dd-mm-yyyy	dd-mm-yyyy			dd-mm-yyyy
Work Awarded / LOA Issued NOTE: Only One PDF file can be uploaded. File Size: Max. 10 MB.					
Awarded Project Cost (In Cr) * 	dd-mm-yyyy	dd-mm-yyyy			dd-mm-yyyy
Contract Agreement Signed NOTE: Only One PDF file can be uploaded. File Size: Max. 10 MB.	dd-mm-yyyy	dd-mm-yyyy			dd-mm-yyyy

Save
Exit

Previous
Next

Figure 15: Under Tendering Data - 2

Input the revised Target Completion Date.

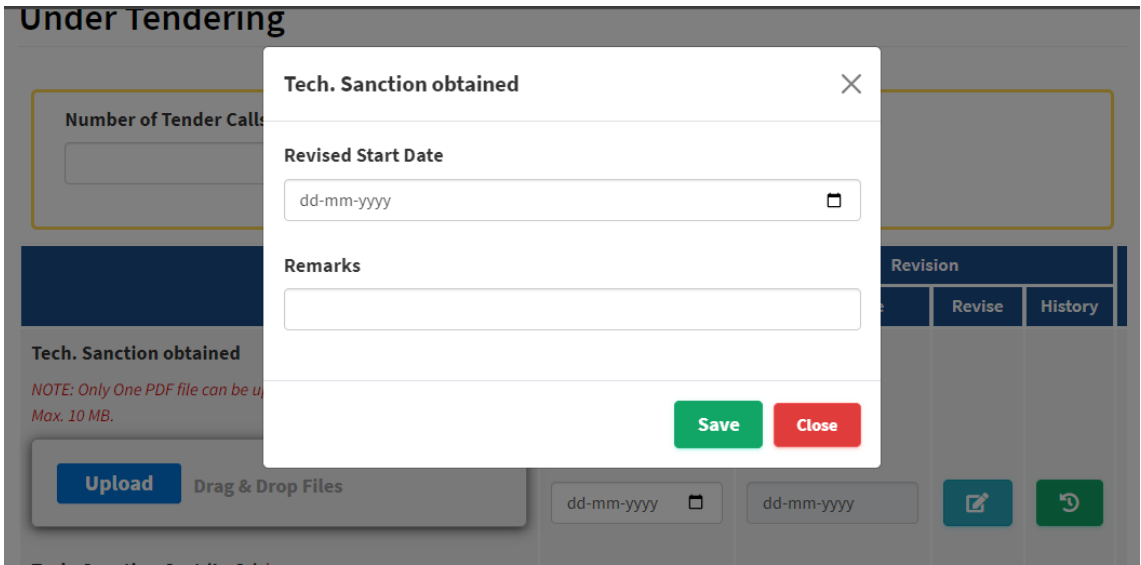


Figure 16: Entering Revised Target Completion Date

If the Revised Target Completion Date is prior to the date already entered a confirmation is made before storing the revised date

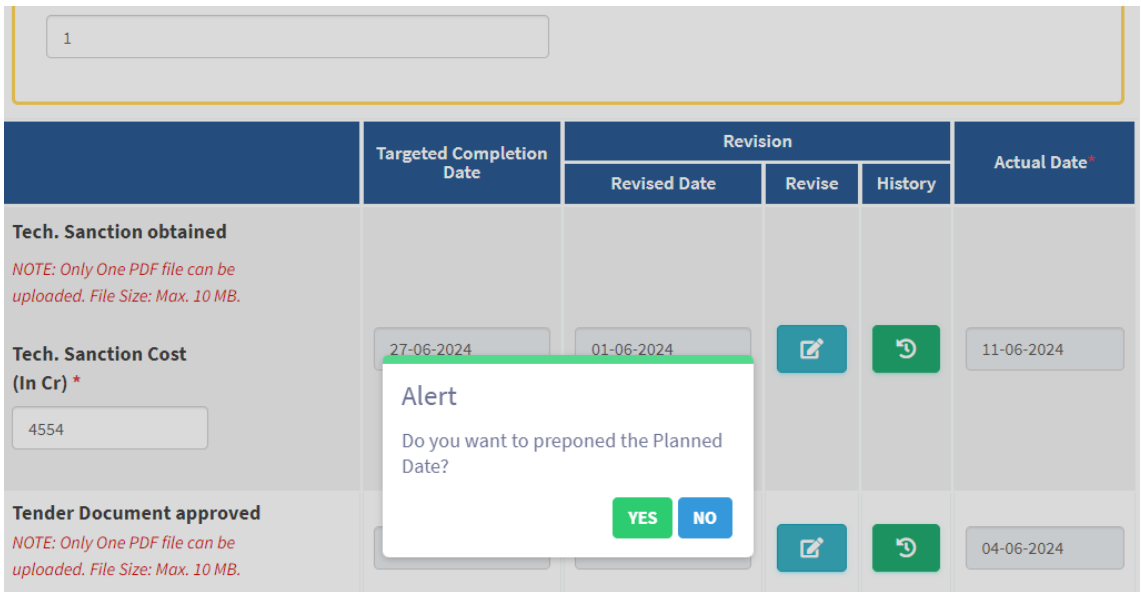


Figure 17: Checking Preponed Target Completion Date

Revised Target Completion Date can be listed by pressing the history icon

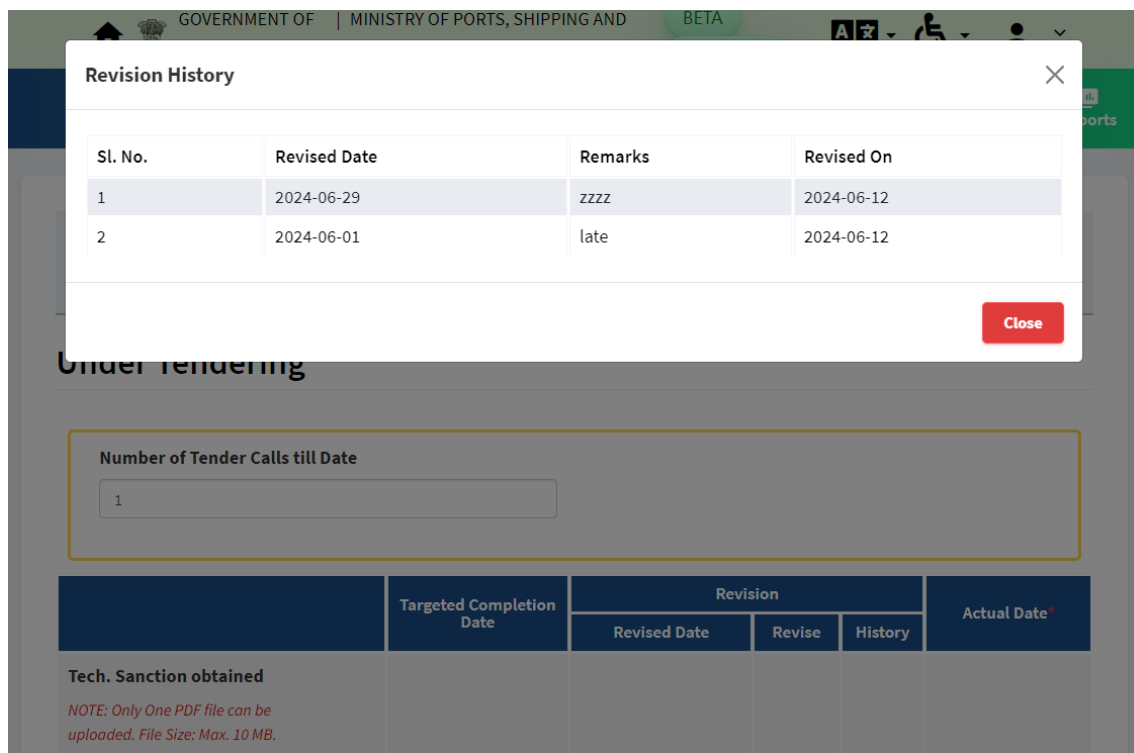


Figure 18: Listing of Revised Target completion Dates

7 Under Implementation

In Under Implementation stage the work progress of the project is entered

On entering the percentage of work progress the data in appropriate milestone gets updated as shown below.

Milestone Monitoring

Physical progress as on*

12-06-2024

(in percentage)*

25

%

Edit

Cancel

Save

Milestone	Targeted End Date	Actual End Date*
Milestone 0 (<20%)	dd-mm-yyyy	dd-mm-yyyy
Milestone 1 (>= 20 <40)	dd-mm-yyyy	dd-mm-yyyy
Milestone 2 (>= 40 <60)	dd-mm-yyyy	dd-mm-yyyy
Milestone 3 (>= 60 <80)	dd-mm-yyyy	dd-mm-yyyy

Figure 19: Entering Percentage of Work Completed

1 Basic Information

2 Planning and Sanctioning

3 Clearances

4 Under Tendering

5 Under Implementation

6 Project Completion

Physical progress as on*

12-06-2024

(in percentage)*

25

%

Edit

Cancel

Save

Milestone	Targeted End Date	Actual End Date*
Milestone 0 (<20%)	dd-mm-yyyy	dd-mm-yyyy
Milestone 1 (>= 20 <40)	dd-mm-yyyy	12-06-2024

Figure 20: 7-Milestone Achieved is Updated Automatically

The percentage progress need to always greater than the previous progress present. Only after 100 percentage progress is achieved the project completion stage will be

Milestone Monitoring

Physical progress as on*

01-05-2024

(in percentage)*

50

%

Edit

Cancel

Save

Physical Progress percentage should be greater than previous value

Milestone	Targeted End Date	Actual End Date*
Milestone 0 (<20%)	dd-mm-yyyy	dd-mm-yyyy
Milestone 1 (>= 20 <40)	dd-mm-yyyy	28-05-2024
Milestone 2 (>= 40 <60)	dd-mm-yyyy	01-06-2024

Figure 21: Alert for Percentage progress to be greater than previous value reached.The Reason for delay also can be mentioned.

Physical progress as on*

12-06-2024

(in percentage)*

100

%

Edit

Cancel

Save

Milestone	Targeted End Date	Actual End Date*
Milestone 0 (<20%)	dd-mm-yyyy	dd-mm-yyyy
Milestone 1 (>= 20 <40)	dd-mm-yyyy	30-05-2024
Milestone 2 (>= 40 <60)	dd-mm-yyyy	03-06-2024
Milestone 3 (>= 60 <80)	dd-mm-yyyy	08-06-2024
Milestone 4 (>= 80 <100)	dd-mm-yyyy	dd-mm-yyyy
Final Milestone (Completion Report) (=100%)	dd-mm-yyyy	12-06-2024

Reasons for Delay(if any):

Figure 22: 100 percentage work progress

In the Expenditure log section the Expenditure details and the expenditure overlay

can be entered .

The screenshot displays a web application interface for 'Expenditure Logs'. At the top, there is a text input field labeled 'Reasons for Delay(if any):'. To its right, a green notification box with a checkmark icon states 'Activity Timeline Updated Successfully'. Below the input field, a horizontal scrollbar is visible. Another green notification box with a checkmark icon states 'Expenditure details saved successfully'. The main section is titled 'Expenditure Logs'. Below the title, there are two status bars: 'Project Cost: 455 Crores' (green) and 'Expenditure Till Date: 76 Crores' (orange). To the right of these are two buttons: 'Expenditure Outlay' (blue) and 'View Expenditure Log' (blue). Below these buttons, there are two dropdown menus: 'Financial Year*' with '2015-2016' selected, and 'Month*' with 'June' selected. Below the dropdowns, there is a text input field labeled 'IEBR Components (In Cr.):' and a green notification box with a checkmark icon stating 'Component Fund: Expenditure Till Date: 76 Crores'. At the bottom left, there are two buttons: 'Save' (green) and 'Exit' (red). At the bottom right, there are two buttons: 'Previous' (blue) and 'Next' (orange).

Figure 23: Expenditure Details entered are saved

In the Expenditure log section the Expenditure overlay can viewed and new values entered .

Expenditure Overlay

Show 10 entries

Copy Excel PDF

S.No Financial Year

1 2023-2024

Showing 1 to 1 of 1 entries

Financial Year*

--Select Financial Year--

Expenditure Outlay (In Crore)*

Submit Cancel

Add Details

Edit

Update

Previous 1 Next

Close

IEBR Components (In Cr.):

Component Fund: Expenditure Till Date: 76 Crores

Figure 24: Adding Expenditure Overlay details

In the Expenditure log section the Expenditure overlay values are listed .

Expenditure Overlay

Show 10 entries

Search:

Copy Excel PDF Column visibility

S.No Financial Year Expenditure Outlay (In Cr.) Edit

1 2023-2024 12345

Showing 1 to 1 of 1 entries

Previous 1 Next

Close

IEBR Components (In Cr.):

Component Fund: Expenditure Till Date: 76 Crores

Figure 25: Expenditure Overlay Listed

In the Expenditure log section the Expenditure overlay can also be updated using update button in the list .

Expenditure Outlay		Edit Details					
Show 10 entries Copy Excel PDF		Financial Year* 2023-2024					
<table border="1"> <thead> <tr> <th>S.No</th> <th>Financial Year</th> </tr> </thead> <tbody> <tr> <td>1</td> <td>2023-2024</td> </tr> </tbody> </table>		S.No	Financial Year	1	2023-2024	Expenditure Outlay (In Crore)* 12345	
S.No	Financial Year						
1	2023-2024						
Showing 1 to 1 of 1 entries		Submit Cancel					

1

Figure 26: Updating Expenditure Overlay details

8 Project Completion

In the Final stage of Project Completion the Project Completion date and Closure Cost is to be entered

1 Basic Information
2 Planning and Sanctioning
3 Clearances
4 Under Tendering
5 Under Implementation
6 Project Completion

Project Completion

Actual Date of Completion*

Closure Cost (In Crore)*

Figure 27: Project Completed Stage

9 Drop a Project

A project can be dropped at any stage except after completion. The reason for canceling the project is to be mentioned and it remains in pending state until the cancellation is

finally approved by the ministry.

While making the drop request of a project the request reason shown below.

The screenshot shows a web form titled 'Land Detail'. It has two main sections: 'Land Detail' and 'Others'. In the 'Land Detail' section, there is a radio button for 'Is Land Acquisition required for Project?' with 'No' selected, and a text input for 'Percent of Land Acquired'. In the 'Others' section, there are two upload areas: 'Project PPT' and 'Latest Project Image', both with 'Upload' buttons and 'Drag & Drop Files' text. A modal alert dialog is open in the center, asking 'Are you sure that you want to request to drop this project?' with a 'Reason' text input and 'REQUEST' and 'CANCEL' buttons. At the bottom of the form, there are 'Update', 'Drop', and 'Exit' buttons, and a 'Next' button in the bottom right corner.

Figure 28: Drop Request Reason

The list of dropped projects is shown below.

The screenshot shows a web application interface with a top navigation bar containing 'Project List', 'Dropped Project List' (active), and 'Reports'. Below the navigation bar is a 'View Drop Requests' section with a search bar and a table. The table has columns for S.No, Project ID, Sub Project ID, Project Name, Sub Project Name, Submitted By, Submitted On, Reason, and Action. The table contains 6 rows of data, with the last row marked as 'Dropped'.

S.No	Project ID	Sub Project ID	Project Name	Sub Project Name	Submitted By	Submitted On	Reason	Action
1	PR0653	-	tywetw	-	test	2024-06-09	xyz	Drop pending
2	PR0653	-	tywetw	-	test	2024-06-09	kjhjij	Drop pending
3	PR0134	-	Dredging the dock basin in front of north cargo III to (-) 15.10m for handling of vessels up to 14.20m draught	-	Ramdulal Mohapatra	2024-05-24	Already listed in serial no 2	Drop pending
4	PR0637	-	Operation & Maintenance of Hemnagar LC Station during 2023-24.	-	Samrat Rahi	2024-05-16	Duplicate entry	Drop pending
5	PR0637	-	Operation & Maintenance of Hemnagar LC Station during 2023-24.	-	Samrat Rahi	2024-05-16	Duplicate entry	Drop pending
6	PR0327	-	Construction of Single lane bridge across TS canal of Nw-3 at Kovilthottam Chavra Kollam	-	Sanjay Bandopadhyay	2024-04-03	DUPLICATE	Dropped

Figure 29: List of Dropped Projects

10 Reports

The Sagarmanthan web portal has various reports catering to the needs of the port users and the ministry users. All reports can be filtered by Organization Category, Organization, Category and Scheme wise Data.

10.1 Report No.: P.1.0 - Abstract - Status of Planning Sanctioning of Projects

Report No.: P.1.0 - Abstract - Status of Planning & Sanctioning of Projects

As On date: 01-04-2024

(Report For the Year 2024-2025)

Organisation Category

Major Ports

Organisation

Show All

Category

Show All

Scheme Wise Data

Show All

Search:

S.No	Organisations	Category	01.04.2014 to 31-03-2024				No.of. Balance ongoing Projects including SubProjects at the beginning of the year (01.04.2024)	Total Estimated cost of balance ongoing Projects including SubProjects (In Cr.)
			No. of Projects including SubProjects taken up	No. of Projects including SubProjects dropped	No. of Projects including SubProjects completed	Total Cost of completed Projects including SubProjects (In Cr.)		
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(9)
1	Chennai Port Authority	PPP/Captive	-	-	-	0	-	0
2	Chennai Port Authority	EPC/Others	16	-	6	113.93	10	273.96
3	Chennai Port Authority	TOTAL	16	-	6	113.93	10	273.96
4	Cochin Port Authority	PPP/Captive	-	-	-	0	-	0
5	Cochin Port Authority	EPC/Others	6	-	2	79.92	4	140.17
6	Cochin Port Authority	TOTAL	6	-	2	79.92	4	140.17

Figure 30: Report No.: P.1.0 - Abstract - Status of Planning Sanctioning of Projects

10.2 Report No.: P.1.1A - Abstract - Status of Planning Sanction of Projects

In Report No.: P.1.1A the port user gets Abstract - Status of Planning Sanction of Projects as shown below.

Report No.: P.1.1A - Abstract - Status of Planning & Sanction of Projects

As On date: 31-05-2024

(Report for the Month - June 2024)

Organisation Category Major Ports	Organisation Show All	Category Show All
--------------------------------------	--------------------------	----------------------

Scheme Wise Data

--Show All--

Search:

S.No	Organisations	Category	No. of Balance ongoing Projects including Subprojects as on 01.04.2024	During the Current FY				No. of Projects including Subprojects at different stages								
				No. of projects taken up	No. of projects dropped	Total no. of Projects as on date including Subprojects	Estimated Cost of Projects including Subprojects(In Cr.)	Projects including Subprojects initiated	Preliminary Feasibility/TEFR Report prepared	Estimate / DPR prepared	Chairman / Board Approval	Submitted to Ministry for approval (If required)	DA concurrence obtained	IFW concurrence obtained	Circulated for IMC	Res. Com. recd.
(1) ⁺	(2) ⁺	(3) ⁺	(4) ⁺	(5) ⁺	(6) ⁺	(7) ⁺	(8) ⁺	(A) ⁺	(B) ⁺	(C) ⁺	(D) ⁺	(E) ⁺	(F) ⁺	(G) ⁺	(H) ⁺	(I) ⁺
7	Deendayal Port Authority	PPP/Captive	2	-	-	2	4882.84									
8	Deendayal Port Authority	EPC/Others	20	-	-	20	3071.78		3							
9	Deendayal Port Authority	TOTAL	22	-	-	22	7954.62		3							

Figure 31: Report No.: P.1.1A - Abstract - Status of Planning Sanction of Projects

Report No.: P.1.1B - Detailed - Status of Planning & Sanction of Projects

As On date: 31-05-2024

(Report for the Month - June 2024)

Organisation *	Mode of Implementation *
Deendayal Port Authority	TOTAL

Search:

S.No	Project ID	Name of		Estimated Cost of Projects including Sub Projects	Date on Which												Sa
		Project	Sub Project		Projects including Sub Projects initiated	Preliminary Feasibility/TEFR Report prepared	Estimate / DPR prepared	Chairman / Board Approval	Submitted to Ministry for approval (if required)	DA concurrence obtained	IFW concurrence obtained	Circulated for IMC	Response to Comments received	SFC/DIB/EFC/PIB/DIB/PPPAC	Appraisal by SFC/DIB/EFC/PIB/DIB/PPPAC	Admn. Approval / Estimate Sanction by Comp. Authority	
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(8)	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)
1	PR0451	Development operation and maintenance of Oil jetty No 09 on PPP mode.	-	198.43		30 Jan 2024	-	-	-	-	-	-	-	-	-	-	
2	PR0452	Development operation and maintenance of Oil jetty No 10 on PPP mode	-	199.90		30 Jan 2024	-	-	-	-	-	-	-	-	-	-	

Figure 32: Report No.: P.1.1B - Detailed - Status of Planning Sanction of Projects

Report No.: P.1.1B - Detailed - Status of Planning Sanction of Projects is obtained (as shown above) when the count ([link](#)) under the respective column is pressed.

10.3 Report No.: P.1.2A - Abstract - Status of Projects under Tendering

In Report No.: P.1.2A the port user gets Abstract - Status of Projects under Tendering as shown below.

Report No.: P.1.2A - Abstract - Status of Projects Under Tendering

As On date: **31-05-2024**

(Report for the Month - June 2024)

Organisation Category Major Ports	Organisation Chennai Port Authority	Category Show All
--	--	--

Scheme Wise Data

Search:

S.No	Organisations	Category	Total No. of Approved Projects including Sub Projects	Cost of Administrative Approved Projects including Sub Projects (A A Cost) (In Cr.)	Cost of Approved Projects including Sub Projects as per Technical Sanction (T S Cost) (In Cr.)	No. of Tenders at different stages									Cost of Awards Projects including Sub Projects (Cr.)
						Tender Process Initiated	Tech. Sanction obtained	Tender Document approved	Tender Notice Issued	Technical Evaluation completed	Financial Evaluation completed	Sanction of Competent Authority obtained for Award	Work Awarded / LOA Issued	Contract Agreement Signed	
(1) ↕	(2) ↕	(3) ↕	(4) ↕	(5) ↕	(6) ↕	(A) ↕	(B) ↕	(C) ↕	(D) ↕	(E) ↕	(F) ↕	(G) ↕	(H) ↕	(I) ↕	(7) ↕
1	Chennai Port Authority	PPP/Captive	0	0	0	-	-	-	-	-	-	-	-	-	0
2	Chennai Port Authority	EPC/Others	10	273.96	135.15	-	1	-	-	-	-	-	-	9	171.24

Figure 33: Report No.: P.1.2A - Abstract - Status of Projects under Tendering

Report No.: P.1.2B - Details - Status of Tendering Process of Projects

As On date: **31-05-2024**

(Report for the Month - June 2024)

Organisation * Chennai Port Authority					Mode of Implementation * EPC+Others														
--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--	--

Search:

S.No	Project Code/ID	Name of		No. of tender calls done	Date on Which																Awarded Cost (In Cr.)		
		Main Project	Sub-Project		Pre Tender Work				Status of Latest Tender Call														
					Tech. Sanction obtained		Tender Document approved		Tender Notice Issued		Technical Evaluation completed		Financial Evaluation completed		Sanction of Competent Authority obtained for Award		Work Awarded / LOA Issued		Contract Agreement Signed				
(1) ↕	(2) ↕	(3) ↕	(4) ↕	(5) ↕	(A) ↕	(A1) ↕	(B) ↕	(B1) ↕	(C) ↕	(C1) ↕	(D) ↕	(D1) ↕	(E) ↕	(E1) ↕	(F) ↕	(F1) ↕	(G) ↕	(G1) ↕	(H) ↕	(H1) ↕	(I) ↕		
1	PR0176	Implementation of EBS (Enterprise Business System)	-	1	-	23 Jan 2018	-	28 Jan 2018	-	02 Feb 2018	-	07 Feb 2018	-	12 Feb 2018	-	17 Feb 2018	-	22 Feb 2018	-	20 Mar 2018	44.46		
2	PR0177	Augmentation of the Existing Fire Fighting system in Oil Dock BD-I and BD-III For	-	1	27 Mar 2024	27 Mar 2024	-	08 Apr 2024	13 Apr 2024	13 Apr 2024	-	09 Nov 2024	-	14 Nov 2024	-	19 Nov 2024	24 Nov 2024	24 Nov 2024	18 Dec 2024	18 Dec 2024	13.49		

Figure 34: Report No.: P.1.2B - Detailed - Status of Tendering process of Projects

Report No.: P.1.2B -Detailed - Status of Tendering process of Projects is obtained (as shown above) when the count [\(link\)](#) under the respective column is pressed.

10.4 Report No.: P.1.3A - Abstract - Status of Implementation of Projects

In Report No.: P.1.3A the port user gets Abstract - Status of Implementation of Projects as shown below.

Report No.: P.1.3A - Abstract - Status of Implementation of Projects

As On date: 31-05-2024

(Report for the Month - June 2024)

Organisation Category Major Ports	Organisation Show All	Category Show All
--------------------------------------	--------------------------	----------------------

Scheme Wise Data

--Show All--

Search:

S.No	Organisations	Category	Total Number of awarded Projects including Sub Projects	Total No. of Projects including Sub Projects for which Agreement signed	No. of Projects including Sub Projects which have crossed					
					Milestone 0 (<20%)	Milestone 1 (>= 20 <40)	Milestone 2 (>= 40 <60)	Milestone 3 (>= 60 <80)	Milestone 4 (>= 80 <100)	Final Milestone (Completion Report) (=100%)
(1)	(2)	(3)	(4)	(5)	(A)	(B)	(C)	(D)	(E)	(F)
1	Chennai Port Authority	PPP/Captive	0	0	-	-	-	-	-	-
2	Chennai Port Authority	EPC/Others	9	9	2	1	1	1	3	1
3	Chennai Port Authority	TOTAL	9	9	2	1	1	1	3	1
4	Cochin Port Authority	PPP/Captive	0	0	-	-	-	-	-	-

Figure 35: Report No.: P.1.3A - Abstract - Status of Implementation of Projects

Report No.: P.1.3B - Details - Status of Implementation of Projects

As On date: 31-05-2024

(Report for the Month - June 2024)

Organisation * Chennai Port Authority	Mode of Implementation * EPC+Others
--	--

Search:

S.No	Project Code	Name of		Date of signing of Agreement	Date of Completion of												Remarks / Action w.r.t. delays, if any.	Photos of project prog
		Main Project	Sub-Project		Milestone 0 (<20%)< /th>		Milestone 1 (>= 20 <40)< /th>		Milestone 2 (>= 40 <60)< /th>		Milestone 3 (>= 60 <80)< /th>		Milestone 4 (>= 80 <100)< /th>		Final Milestone (Completion Report) (=100%)			
					Target	Achieved	Target	Achieved	Target	Achieved	Target	Achieved	Target	Achieved	Target	Achieved		
(1)	(2)	(3)	(4)	(5)	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)	(I)	(J)	(K)	(L)	(7)	(8)
1	PR0177	Augmentation of the Existing Fire Fighting system in Oil Dock BD-I and BD-II for handling ships more than 1,00,000 DWT as per OISD standard 156-2017	-	18 Dec 2023	30 Apr 2024	-	31 May 2024	-	31 Jul 2024	-	30 Sep 2024	-	15 Nov 2024	-	19 Dec 2024	-	-	Photos Augmentation of Fire Fighting 21022024_1604
2	PR0182	Modernisation of Chennai Fishing	-	14 Oct 2022	-	-	-	-	-	-	-	-	-	-	-	-	-	

Figure 36: Report No.: P.1.3B - Detailed - Status of Implementation of Projects

Report No.: P.1.3B -Detailed - Status of Implementation of Projects is obtained (as shown above) when the count [\(link\)](#) under the respective column is pressed.

10.5 Report No.: P.1.4A - Abstract - Status of Physical and Financial Status of Projects

In Report No.: P.1.4A Status of Physical and Financial Status of Projects as shown below.

Report No.: P.1.4A - Abstract - Status of Physical & Financial Progress of Projects

As On date: 31-05-2024

(Report for the Month - June 2024)

Organisation Category	Organisation	Category
Major Ports	Show All	Show All

Scheme Wise Data

--Show All--

Search:

S.No	Organisations	Category	Financial Status at the beging of FY				Physical Progress during the FY				Financial Progress during the FY			
			Cost of the sanctioned Projects including Sub Projects (In Cr.)	Cost of the awarded Projects including Sub Projects (In Cr.)	Expenditure done till 31.03.2024 (In Cr.)	Balance Exp to be made (In Cr.)	Number of Completion Projects including Sub Projects			Value of completed Projects including Sub Projects (In Cr.)	Expenditure (In Rs.)			
							From 1st April of the FY till the beginning of the month	During the month	Total		Proportionate Target (In Cr.)	From 1st April of the FY till the beginning of the month (In Cr.)	During the month (In Cr.)	Total (In Cr.)
(1)	(2)	(3)	(4)	(5)	(6)	(7)	(A)	(B)	(C)	(D)	(E)	(F)	(G)	(H)
1	Chennai Port Authority	PPP/Captive	-	-	-	-	-	-	-	-	-	-	-	-
2	Chennai Port Authority	EPC/Others	584.92	366.07	255.94	110.13	1	-	1	5.91	1.05	-	-	-

Figure 37: Report No.: P.1.4A - Abstract - Status of Physical and Financial Status of Projects

11 Validations and Conditions - Projects

This section of the user manual provide guidelines and instructions on the validations and conditions at various data form input form filling process.

11.1 Basic Information

The primary process in Projects and proposals is to Input the Basic Information The basic Information of a project is filled up normal user credentials . This includes fields like Project Name , Project Type , Project Cost , Implementing agency and so on . The fields marked by * fields. The Project gets created upon pressing save button. If the Project type selected in the basic approval is Port level approval , the approval is done at chairman level hence, the Planning and Sanctioning page is filled by the normal user.

11.2 Planning and Sanctioning

After a project is successfully created by the normal user , further entries can only be done done by the ministry users . When the ministry user (admin logs in the newly created project is visible and the update button is pressed to input the various dates for various stages of the project like Pre-feasiblity , DPR,IFW concurrence obtained etc. This for all project types except Port Level approval. The two fields in Admin Approval/Estimate sanction by Comp. authority namely sanctioned cost and actual date is compulsory.

11.3 Note

If the user has selected Port Level Approval during the first basic information page, then in the planning and sanctioning page there is chairman board approval. The date of approval by chairman is a compulsory entry to go to the next stage.

11.4 Clearances

This stage of project data entry is reached only after ministry user / normal user (depending on normal project type or Port level approval) but is not a mandatory step. Even without the clearance details steps not entered the next stage of data entry is reached. This is because not all projects need to submit or upload clearance documents.

11.5 Under Tendering

In the Under Tendering stage the target completion dates are to be entered. The only one PDF supporting documents with maximum 10 can be uploaded. The awarded project cost and contract agreement sign date is the compulsory field to go from under Tendering to Under Implementation. Only if the said two fields are entered the Under implementation stage will be enabled.

11.6 Under Implementation

Here the physical progress percentage as on date is entered. The milestone and actual end date are automatically calculated from physical percentage if they are not entered previously. Under implementation stays until the physical progress reaches 100 percentage. Unless 100 percentage physical progress is not reached the next stage project completion will not be enable. System does not allow progress percentage any value less than previous milestone entered value.

12 Amendment Details

Revision	Author	Date	Verified By	Approved By
0	Priya Somasundaran	June 14, 2024	Pradhiksha	Dr Raju

13 Distribution List & Contact Details

Name	Designation / Company	E-Mail ID / Mobile No
Priya Somasundaran	Sr. Project Officer NTCPWC,IITM	priya@ntcpwc.iitm.ac.in
Pradhiksha	NTCPWC,IITM	pradhiksha@ntcpwc.iitm.ac.in
